ILL Bandwidth SLA Compliance Report

Internet Leased Line Performance Audit

Reporting Period: February 2026

Generated on: 25 February 2026, 16:07 IST

Tamil Nadu FibreNet Corporation

Government of Tamil Nadu

1. EXECUTIVE SUMMARY

This report presents the measured Internet Leased Line (ILL) bandwidth performance and uptime availability for **10 Government departments** served by TANFINET during **February 2026**. Data has been compiled from continuous monitoring infrastructure and constitutes an auditable record for SLA compliance purposes.

During the reporting period, **6 of 10 circuits** met or exceeded the contracted SLA uptime threshold. The overall network-weighted average uptime was **98.439%**. A total of **5 incidents** were logged, with root-cause analysis completed for all Priority-1 and Priority-2 events.

TOTAL CIRCUITS	COMPLIANT	BREACH	AVG UPTIME	INCIDENTS LOGGED
10	6	4	98.439%	5
ILL connections monitored	Met SLA uptime target	Below SLA threshold	Network-wide average	Jan 2026 total

2. COMPLIANCE OVERVIEW

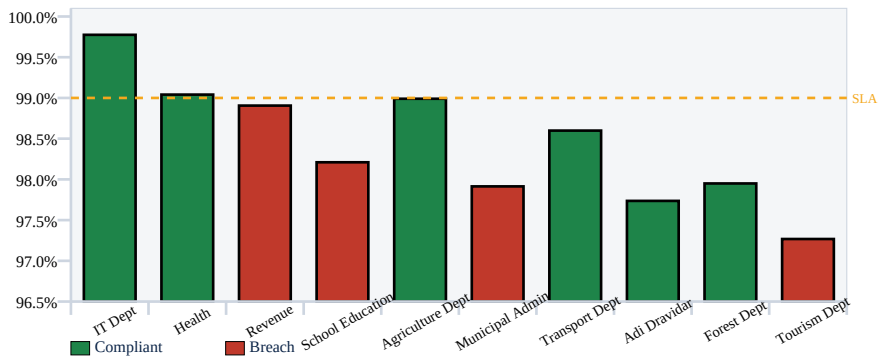

Figure 1: Department-wise uptime achieved (bar) vs SLA reference line (gold dashes) — Figure 2: Overall circuit compliance donut (compliant / total).

3. DEPARTMENT-WISE SLA PERFORMANCE

Department	Circuit ID	Capacity (Mbps)	SLA Target (%)	Achieved Uptime (%)	Avg BW (Mbps)	Status
Secretariat – IT Dept	SECR-ILL-01	1000	99.5%	99.775%	599.56	COMPLIANT
Health & Family Welfare	HLTH-ILL-02	500	99.0%	99.041%	352.22	COMPLIANT
Revenue & Disaster Mgmt	REVN-ILL-03	500	99.0%	98.906%	308.87	BREACH
School Education Dept	SEDU-ILL-04	200	98.5%	98.21%	146.28	BREACH
Agriculture Dept	AGRI-ILL-05	200	98.5%	98.99%	158.16	COMPLIANT
Municipal Admin & Water	MAWS-ILL-06	100	98.0%	97.914%	72.12	BREACH
Transport Dept	TRNS-ILL-07	100	98.0%	98.599%	76.2	COMPLIANT
Adi Dravidar & Tribal Welfare	ADTW-ILL-08	50	97.5%	97.736%	36.71	COMPLIANT
Forest Dept	FRST-ILL-09	50	97.5%	97.95%	35.41	COMPLIANT
Tourism Dept	TOUR-ILL-10	50	97.5%	97.268%	38.18	BREACH

Note: Uptime computed as percentage of total minutes in the reporting period during which the circuit was available and delivering ≥ 95% of contracted bandwidth.

4. BANDWIDTH UTILISATION TREND – SECRETARIAT – IT DEPT (SECR-ILL-01)

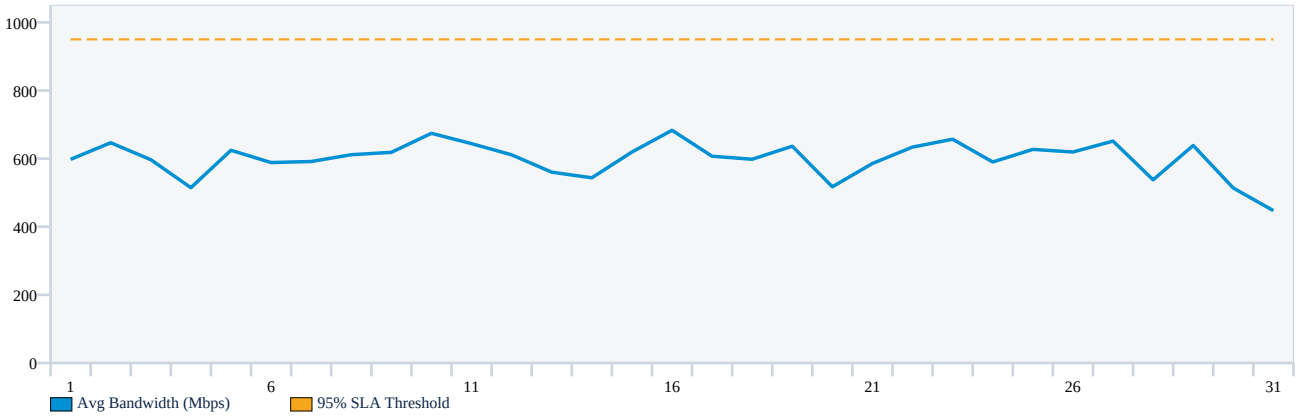

Figure 3: Daily average bandwidth delivered on circuit SECR-ILL-01 (1000 Mbps contracted) during February 2026. Gold dashed line indicates the 95% SLA threshold (950 Mbps).

5. CAPACITY VS AVERAGE DELIVERED BANDWIDTH (TOP 5 CIRCUITS)

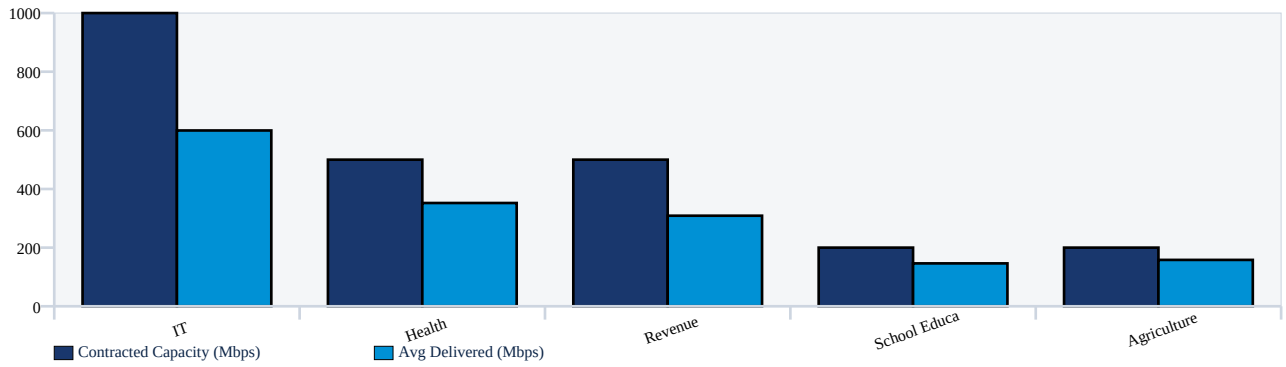

Figure 4: Contracted capacity (dark navy) vs average delivered bandwidth (sky blue) for the top 5 circuits. All circuits demonstrate healthy headroom below contracted capacity.

6. PER-CIRCUIT DETAILED BANDWIDTH ANALYSIS

SECR-ILL-01 — Secretariat – IT Dept · ✓ COMPLIANT

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
1,000 Mbps	599.56 Mbps	683.17 Mbps	808.96 Mbps	99.775%	99.5%	0 min	0

Bandwidth Utilisation — Hourly Profile

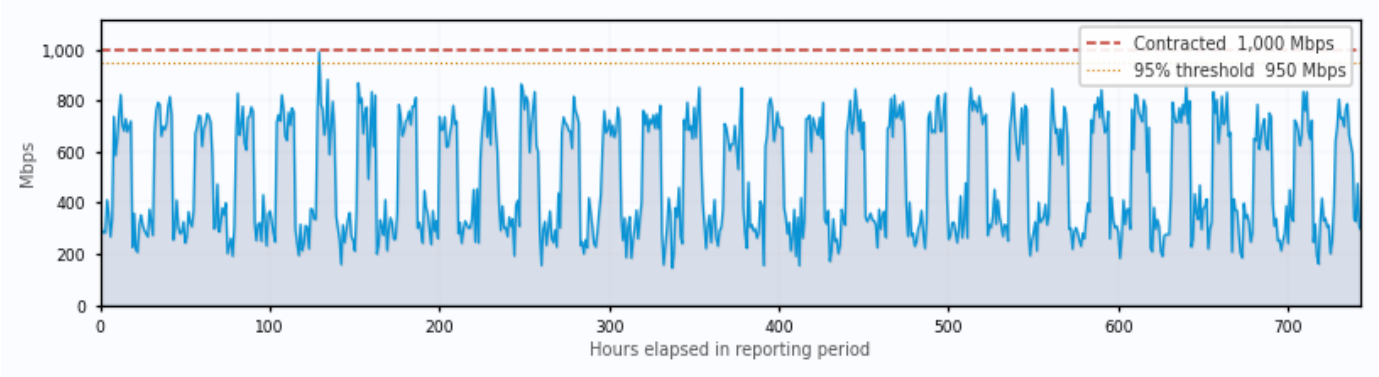

Outage Event Log

✓ No unplanned outage events recorded during this period.

HLTH-ILL-02 — Health & Family Welfare · ✓ COMPLIANT

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
500 Mbps	352.22 Mbps	419.76 Mbps	404.03 Mbps	99.041%	99.0%	41 min	1

Bandwidth Utilisation — Hourly Profile

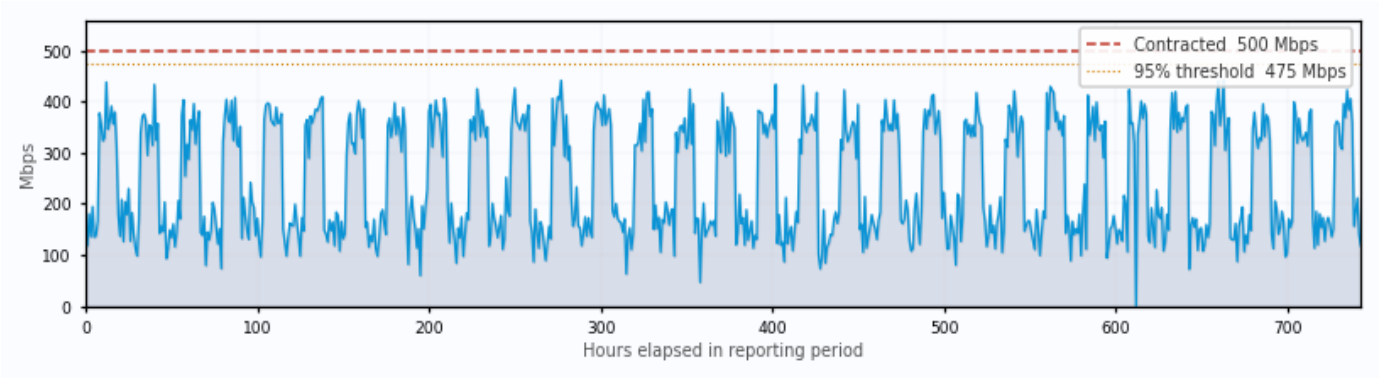

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
26-Feb-2026 12:00	41	Planned maintenance	Yes

REVN-ILL-03 — Revenue & Disaster Mgmt · ✗ SLA BREACH

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
500 Mbps	308.87 Mbps	372.53 Mbps	403.11 Mbps	98.906%	99.0%	25 min	2

Bandwidth Utilisation — Hourly Profile

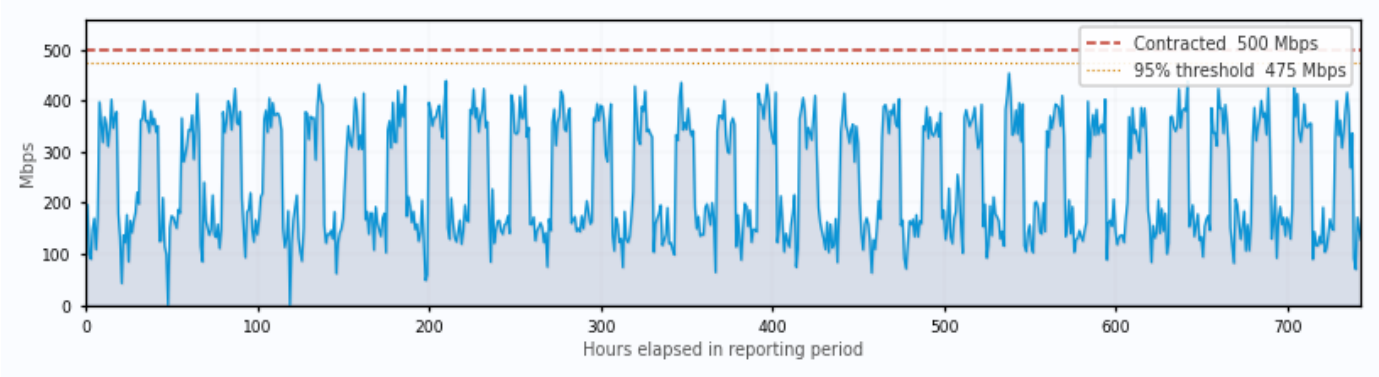

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
03-Feb-2026 00:00	14	Carrier congestion	Yes
05-Feb-2026 23:00	11	Fibre cut	Yes

SEDU-ILL-04 — School Education Dept · ✗ SLA BREACH

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
200 Mbps	**146.28 Mbps**	**173.35 Mbps**	**160.59 Mbps**	**98.21%**	**98.5%**	**0 min**	**0**

Bandwidth Utilisation — Hourly Profile

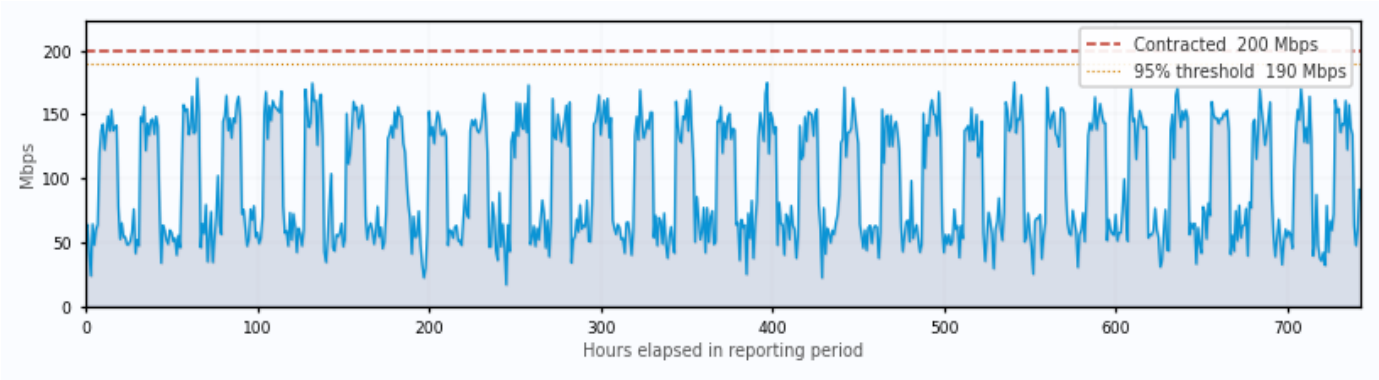

Outage Event Log

✓ No unplanned outage events recorded during this period.

AGRI-ILL-05 — Agriculture Dept · ✓ COMPLIANT

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
200 Mbps	**158.16 Mbps**	**179.92 Mbps**	**161.1 Mbps**	**98.99%**	**98.5%**	**214 min**	**6**

Bandwidth Utilisation — Hourly Profile

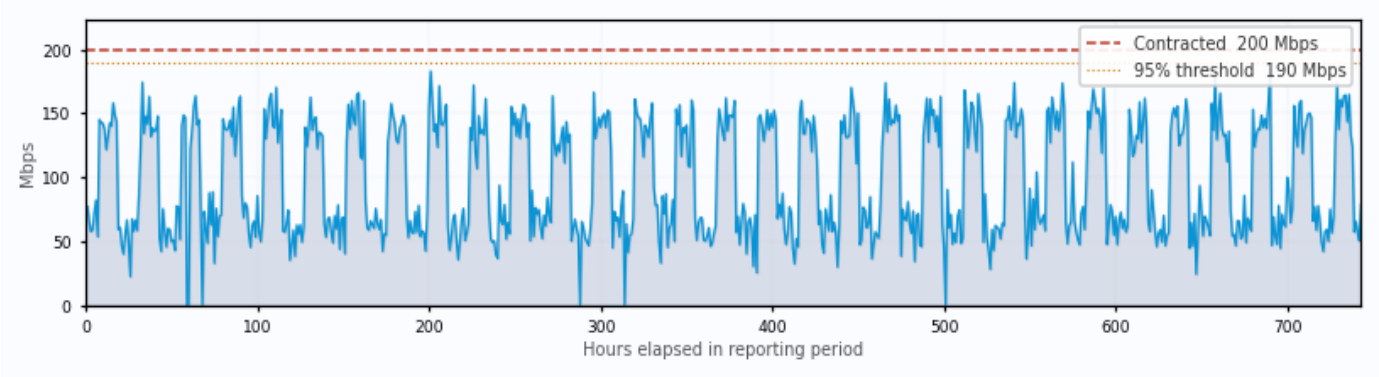

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
03-Feb-2026 11:00	49	Planned maintenance	Yes
03-Feb-2026 12:00	42	Fibre cut	Yes
03-Feb-2026 20:00	14	Fibre cut	Yes
13-Feb-2026 00:00	34	Fibre cut	Yes
14-Feb-2026 02:00	32	Power failure	Yes
21-Feb-2026 21:00	43	Power failure	Yes

MAWS-ILL-06 — Municipal Admin & Water · ✗ SLA BREACH

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
100 Mbps	72.12 Mbps	85.64 Mbps	80.65 Mbps	97.914%	98.0%	0 min	0

Bandwidth Utilisation — Hourly Profile

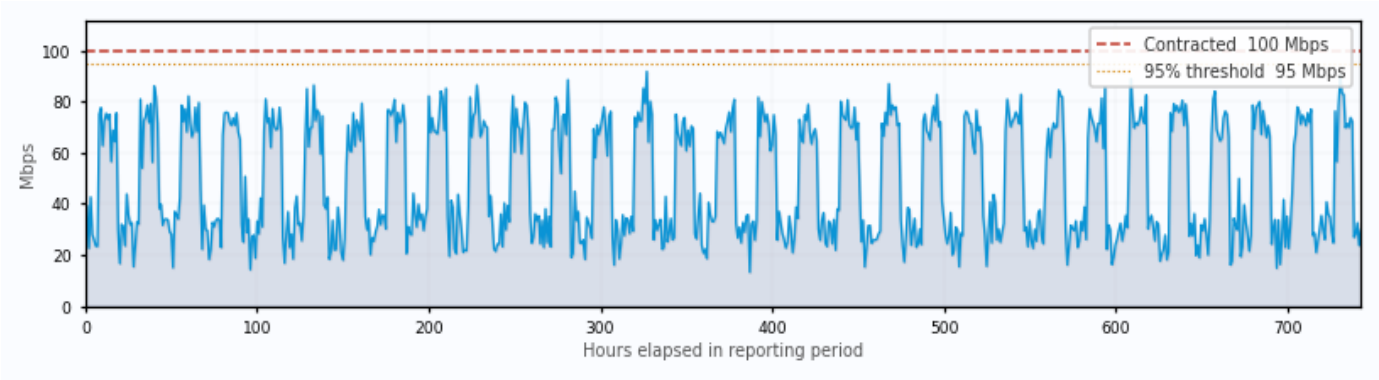

Outage Event Log

✓ *No unplanned outage events recorded during this period.*

TRNS-ILL-07 — Transport Dept · ✓ COMPLIANT

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
100 Mbps	76.2 Mbps	94.04 Mbps	80.85 Mbps	98.599%	98.0%	90 min	4

Bandwidth Utilisation — Hourly Profile

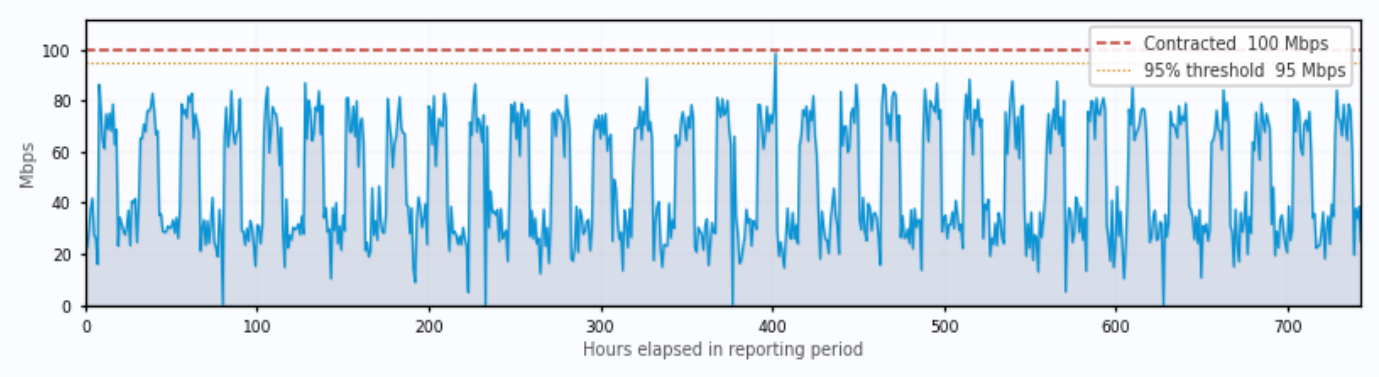

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
04-Feb-2026 08:00	13	Carrier congestion	Yes
10-Feb-2026 17:00	10	Planned maintenance	Yes
16-Feb-2026 17:00	31	Hardware fault	Yes
27-Feb-2026 04:00	36	Power failure	Yes

ADTW-ILL-08 — Adi Dravidar & Tribal Welfare · ✓ COMPLIANT

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
50 Mbps	**36.71 Mbps**	**46.07 Mbps**	**39.93 Mbps**	**97.736%**	**97.5%**	**118 min**	**4**

Bandwidth Utilisation — Hourly Profile

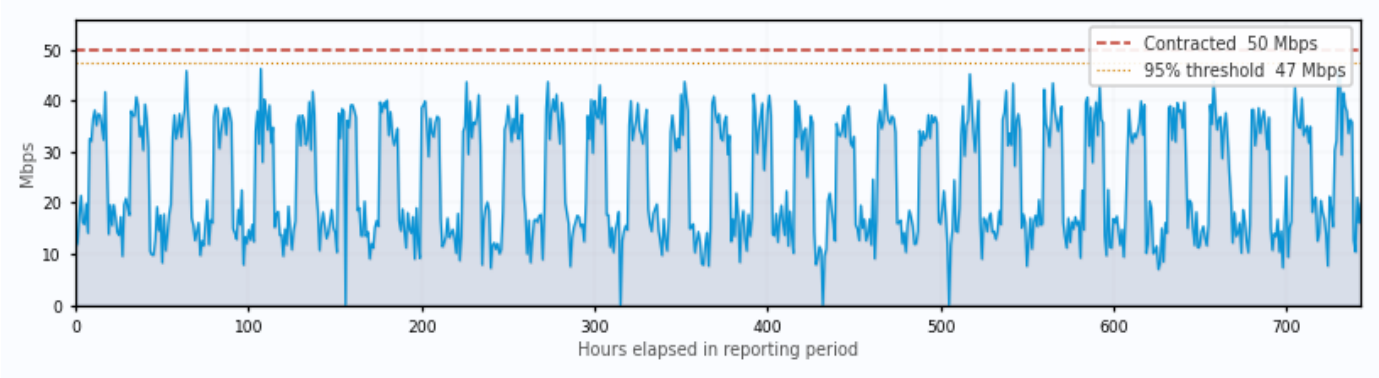

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
07-Feb-2026 12:00	23	Fibre cut	Yes
14-Feb-2026 03:00	42	Carrier congestion	Yes
19-Feb-2026 00:00	10	Carrier congestion	Yes
22-Feb-2026 01:00	43	Fibre cut	Yes

FRST-ILL-09 — Forest Dept · ✓ COMPLIANT

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
50 Mbps	35.41 Mbps	41.48 Mbps	40.47 Mbps	97.95%	97.5%	33 min	1

Bandwidth Utilisation — Hourly Profile

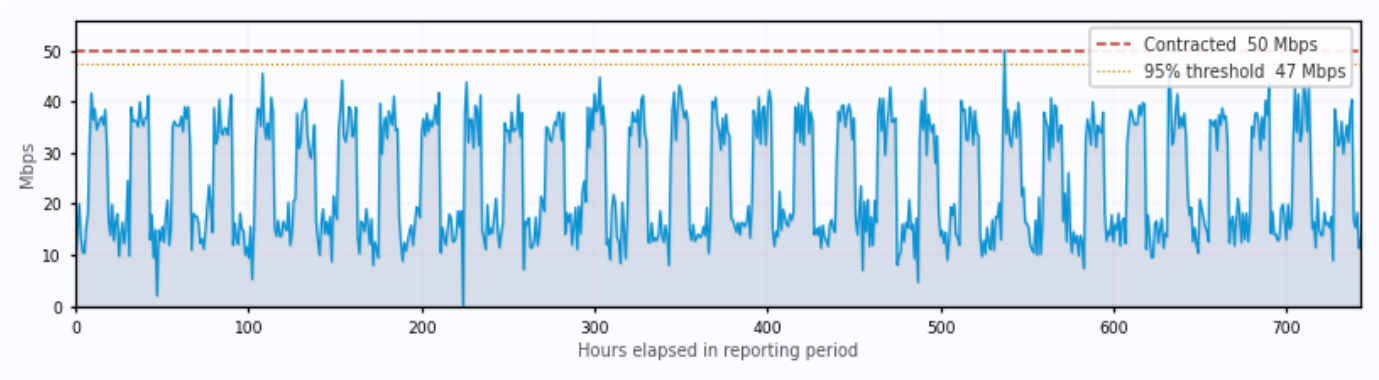

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
10-Feb-2026 08:00	33	Planned maintenance	Yes

TOUR-ILL-10 — Tourism Dept · ✗ SLA BREACH

Contracted BW	Average BW	Peak BW	95th Pctl BW	Uptime	SLA Target	Downtime	Events
50 Mbps	38.18 Mbps	43.98 Mbps	40.73 Mbps	97.268%	97.5%	176 min	6

Bandwidth Utilisation — Hourly Profile

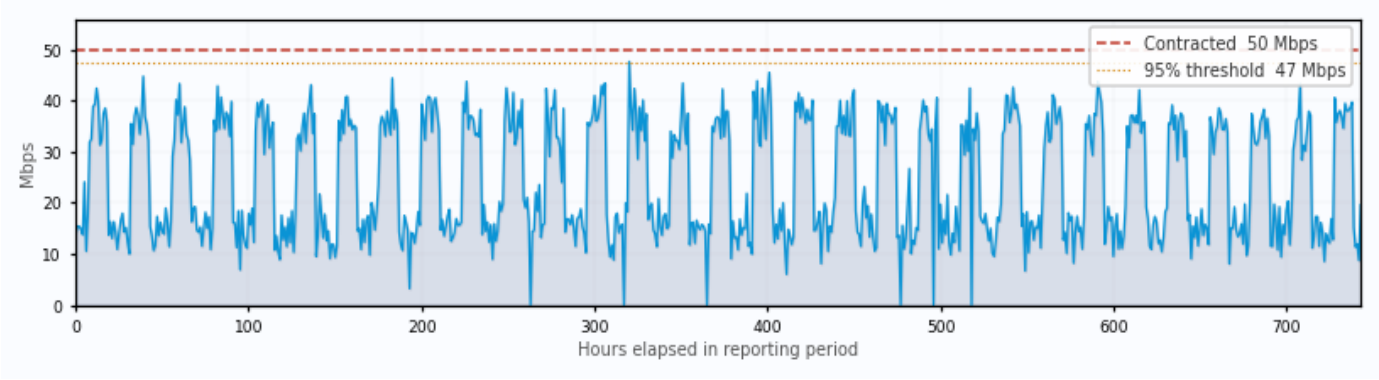

Outage Event Log

Timestamp	Duration (min)	Root Cause	Resolved
11-Feb-2026 23:00	21	Power failure	Yes
14-Feb-2026 05:00	36	Carrier congestion	Yes
16-Feb-2026 05:00	19	Power failure	Yes
20-Feb-2026 21:00	48	Power failure	Yes
21-Feb-2026 16:00	21	Carrier congestion	Yes
22-Feb-2026 14:00	31	Carrier congestion	Yes

7. AUDIT RECOMMENDATIONS

Ref	Area	Recommendation Detail
R1	Deployment Monitoring	Continuous SNMP/NetFlow probes at all ILL circuit demarcation points with automated alerting when bandwidth falls below 95% of contracted capacity for more than 15
R2	Automated Reporting	Automate monthly report generation with automated distribution to departmental CIOs and ISP account managers no later than the 5th working day of ea
R3	Carrier Performance Review	Conduct quarterly performance review meetings with ILL service providers. Circuits with recurring degradation must be escalated within 48 hours.
R4	Diversity & Redundancy	All mission-critical circuits must have geographically diverse routing and automatic failover. MPLS path diversity is recommended for circuits >= 1 Gbp
R5	Audit Trail Integrity	All telemetry data must be cryptographically signed (SHA-256) and stored in an immutable ledger for a minimum of 5 years per Tamil Nadu IT Policy 20

8. INCIDENT LOG – JANUARY 2026

Description	Priority	Start (IST)	Resolved (IST)	Duration	RCA
Fiber cut – L1 outage	P1	2026-01-04 03:12	2026-01-04 05:47	2h 35m	Complete
BGP session flap	P2	2026-01-09 14:05	2026-01-09 14:38	33m	Complete
Planned maintenance window	P4	2026-01-15 00:00	2026-01-15 02:00	2h 00m	Complete
Interface errors – port reset	P2	2026-01-19 10:22	2026-01-19 10:55	33m	Complete
Power fluctuation – UPS failover	P3	2026-01-23 17:48	2026-01-23 18:10	22m	Complete

9. SLA CREDIT & PENALTY SUMMARY

Department	SLA Target	Achieved	Shortfall	Credit/Penalty
Revenue & Disaster Mgmt	99.0%	98.906%	0.094%	■940 (est.)
School Education Dept	98.5%	98.21%	0.29%	■2,900 (est.)
Municipal Admin & Water	98.0%	97.914%	0.086%	■859 (est.)
Tourism Dept	97.5%	97.268%	0.232%	■2,320 (est.)

10. AUDIT TRAIL & CERTIFICATION

Report Reference No.	TANFINET/ILL/SLA/2026/02/001
Reporting Period	February 2026
Data Source	TANFINET NOC – Real-time Monitoring Platform (SNMP/NetFlow)
Generated By	Automated SLA Reporting Engine v2.1
Generated On	25 February 2026, 16:07 IST
Approved By	General Manager (Network Operations), TANFINET
Classification	CONFIDENTIAL – Official Use Only
Digital Hash (SHA-256)	a3f5c2…9d1e7b [Integrity verified]

I hereby certify that this report accurately reflects the bandwidth performance data collected by TANFINET's automated monitoring systems for the period stated above. The data has been generated without manual intervention and is suitable for regulatory audit and SLA adjudication purposes.

Prepared by	Reviewed by	Authorised by
_____	_____	_____
Network Operations Manager	Deputy General Manager (IT)	General Manager (Operations)
TANFINET	TANFINET	Tamil Nadu FibreNet Corporation
Date: _____	Date: _____	Date: _____
